


SR50 PROJECTS (West)

as of 2/23/12

NOTE:
 - Dollar amounts are in millions.
 - Dollar amounts for unfunded phases are PDC (Present day const).
 - Dollar amounts for funded phases are calculated to the funded year.
 - Based on the tentative work program.

HIGHEST PROGRAMMED PHASE

PHASE	COLOR
P.D. & E.	
PREL. ENG.	
RIGHT OF WAY	
CONSTRUCTION	

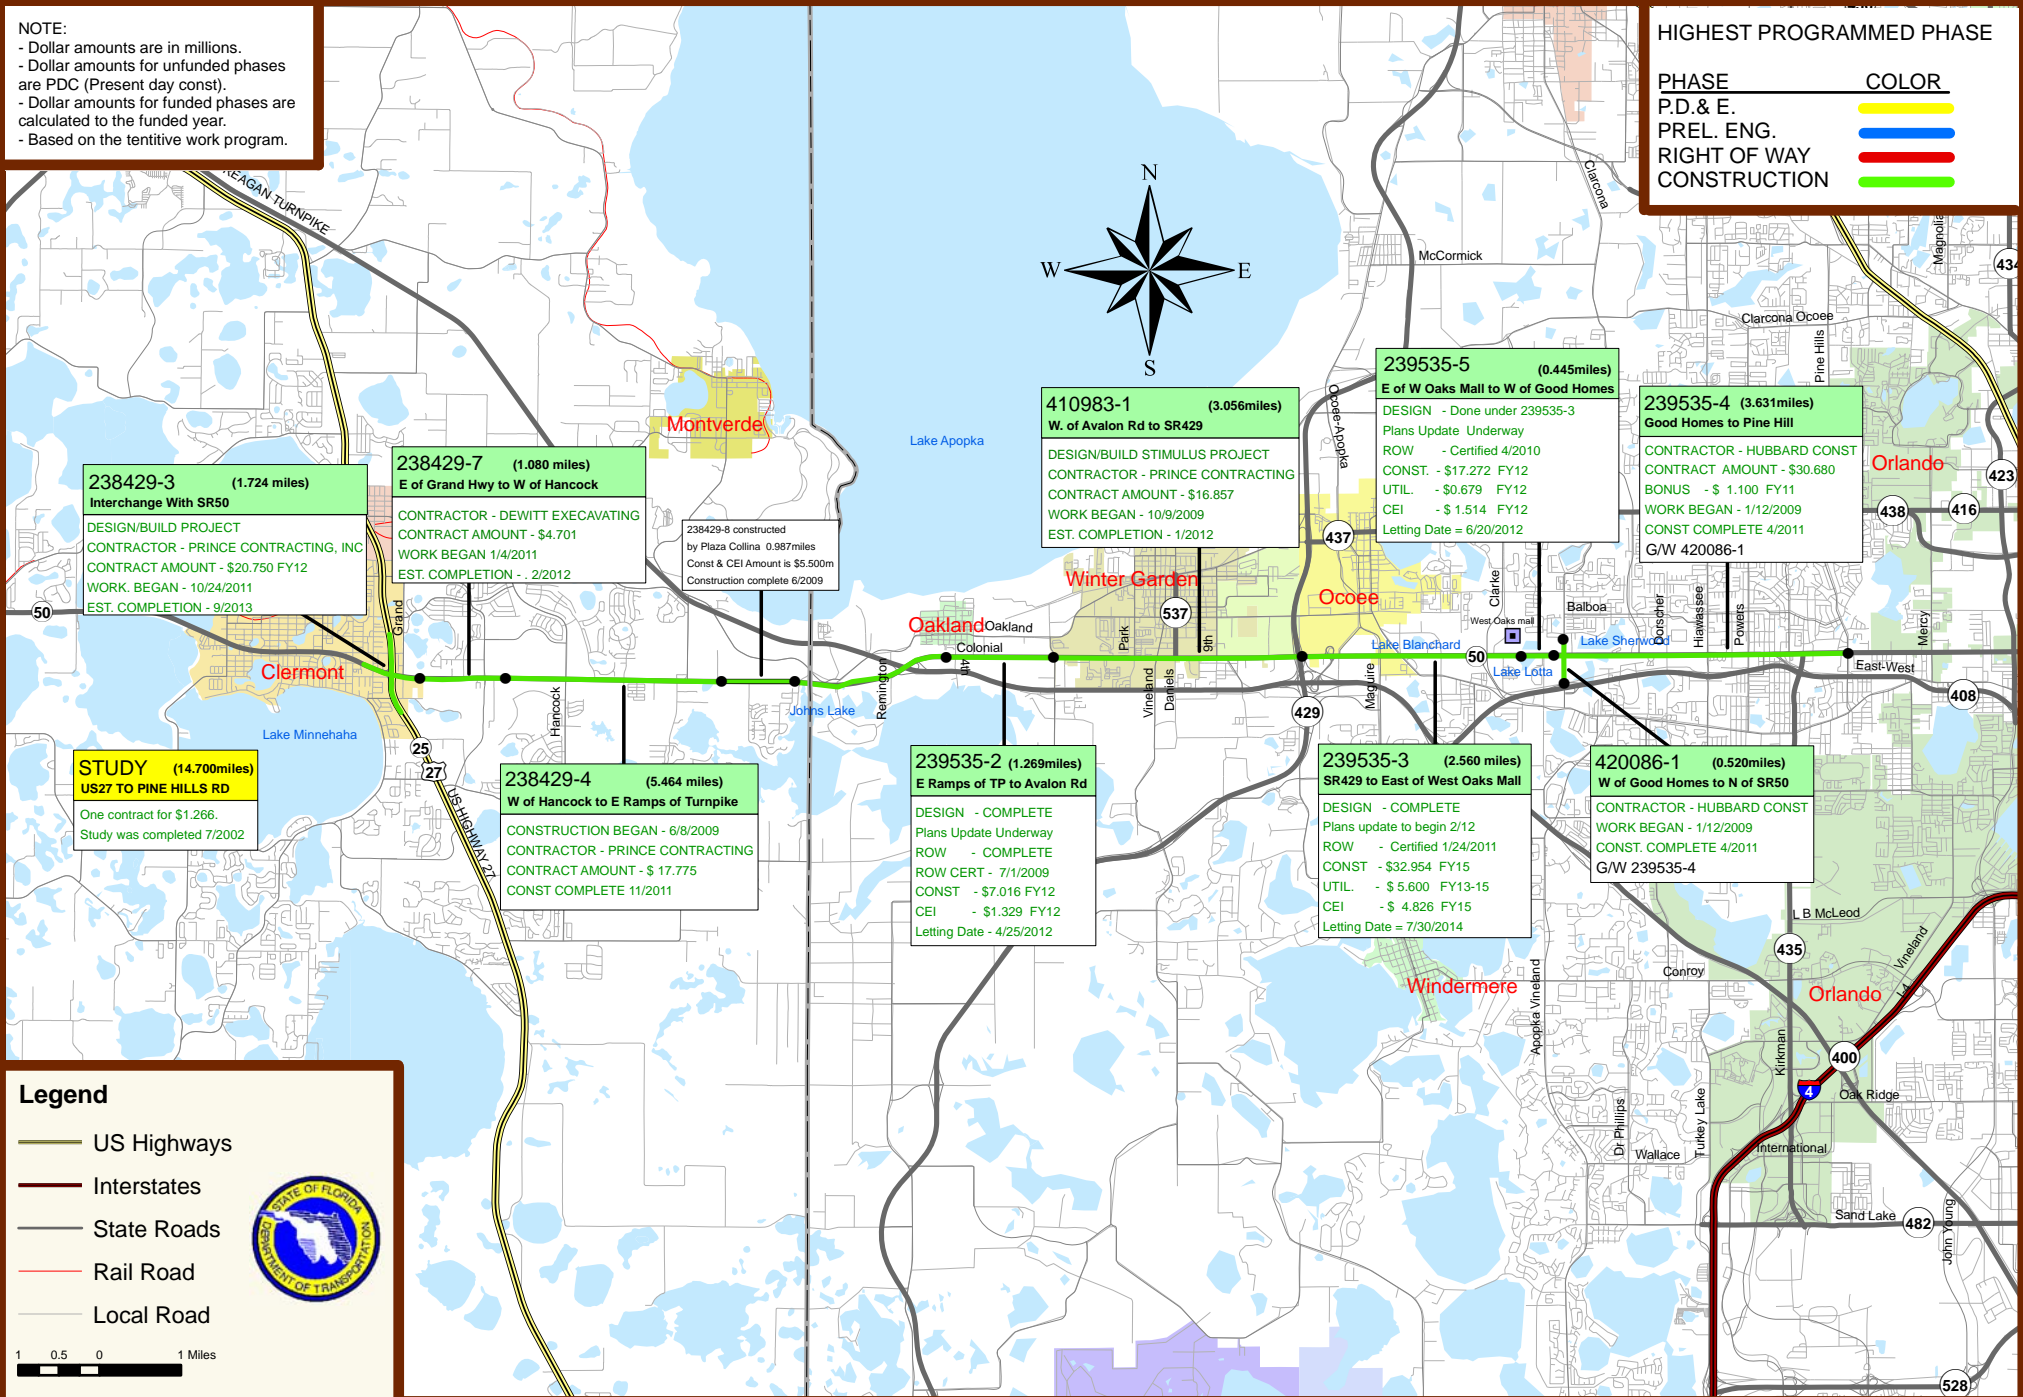

238429-3 (1.724 miles)
Interchange With SR50
 DESIGN/BUILD PROJECT
 CONTRACTOR - PRINCE CONTRACTING, INC
 CONTRACT AMOUNT - \$20.750 FY12
 WORK BEGAN - 10/24/2011
 EST. COMPLETION - 9/2013

238429-7 (1.080 miles)
E of Grand Hwy to W of Hancock
 CONTRACTOR - DEWITT EXCAVATING
 CONTRACT AMOUNT - \$4.701
 WORK BEGAN 1/4/2011
 EST. COMPLETION - 2/2012

238429-8 constructed by Plaza Collina 0.987miles Const & CEI Amount is \$5.500m Construction complete 6/2009

410983-1 (3.056miles)
W. of Avalon Rd to SR429
 DESIGN/BUILD STIMULUS PROJECT
 CONTRACTOR - PRINCE CONTRACTING
 CONTRACT AMOUNT - \$16.857
 WORK BEGAN - 10/9/2009
 EST. COMPLETION - 1/2012

239535-5 (0.445miles)
E of W Oaks Mall to W of Good Homes
 DESIGN - Done under 239535-3
 Plans Update Underway
 ROW - Certified 4/2010
 CONST. - \$17.272 FY12
 UTIL. - \$0.679 FY12
 CEI - \$ 1.514 FY12
 Letting Date = 6/20/2012

239535-4 (3.631miles)
Good Homes to Pine Hill
 CONTRACTOR - HUBBARD CONST
 CONTRACT AMOUNT - \$30.680
 BONUS - \$ 1.100 FY11
 WORK BEGAN - 1/12/2009
 CONST COMPLETE 4/2011
 G/W 420086-1

STUDY (14.700miles)
US27 TO PINE HILLS RD
 One contract for \$1.266.
 Study was completed 7/2002

238429-4 (5.464 miles)
W of Hancock to E Ramps of Turnpike
 CONSTRUCTION BEGAN - 6/8/2009
 CONTRACTOR - PRINCE CONTRACTING
 CONTRACT AMOUNT - \$ 17.775
 CONST COMPLETE 11/2011

239535-2 (1.269miles)
E Ramps of TP to Avalon Rd
 DESIGN - COMPLETE
 Plans Update Underway
 ROW - COMPLETE
 ROW CERT - 7/1/2009
 CONST - \$7.016 FY12
 CEI - \$1.329 FY12
 Letting Date - 4/25/2012

239535-3 (2.560 miles)
SR429 to East of West Oaks Mall
 DESIGN - COMPLETE
 Plans update to begin 2/12
 ROW - Certified 1/24/2011
 CONST - \$32.954 FY15
 UTIL. - \$ 5.600 FY13-15
 CEI - \$ 4.826 FY15
 Letting Date = 7/30/2014

420086-1 (0.520miles)
W of Good Homes to N of SR50
 CONTRACTOR - HUBBARD CONST
 WORK BEGAN - 1/12/2009
 CONST. COMPLETE 4/2011
 G/W 239535-4

- Legend**
- US Highways
 - Interstates
 - State Roads
 - Rail Road
 - Local Road

