



SR40 PROJECTS

as of 1/13/12

NOTE:
 - Dollar amounts are in millions.
 - Dollar amounts for unfunded phases are PDC (Present day const).
 - Dollar amounts for funded phases are calculated to the funded year.
 - Based on the tentative work program.

HIGHEST PROGRAMMED PHASE

| PHASE | COLOR |
|--------------|-------|
| P.D. & E. | |
| PREL. ENG. | |
| RIGHT OF WAY | |
| CONSTRUCTION | |

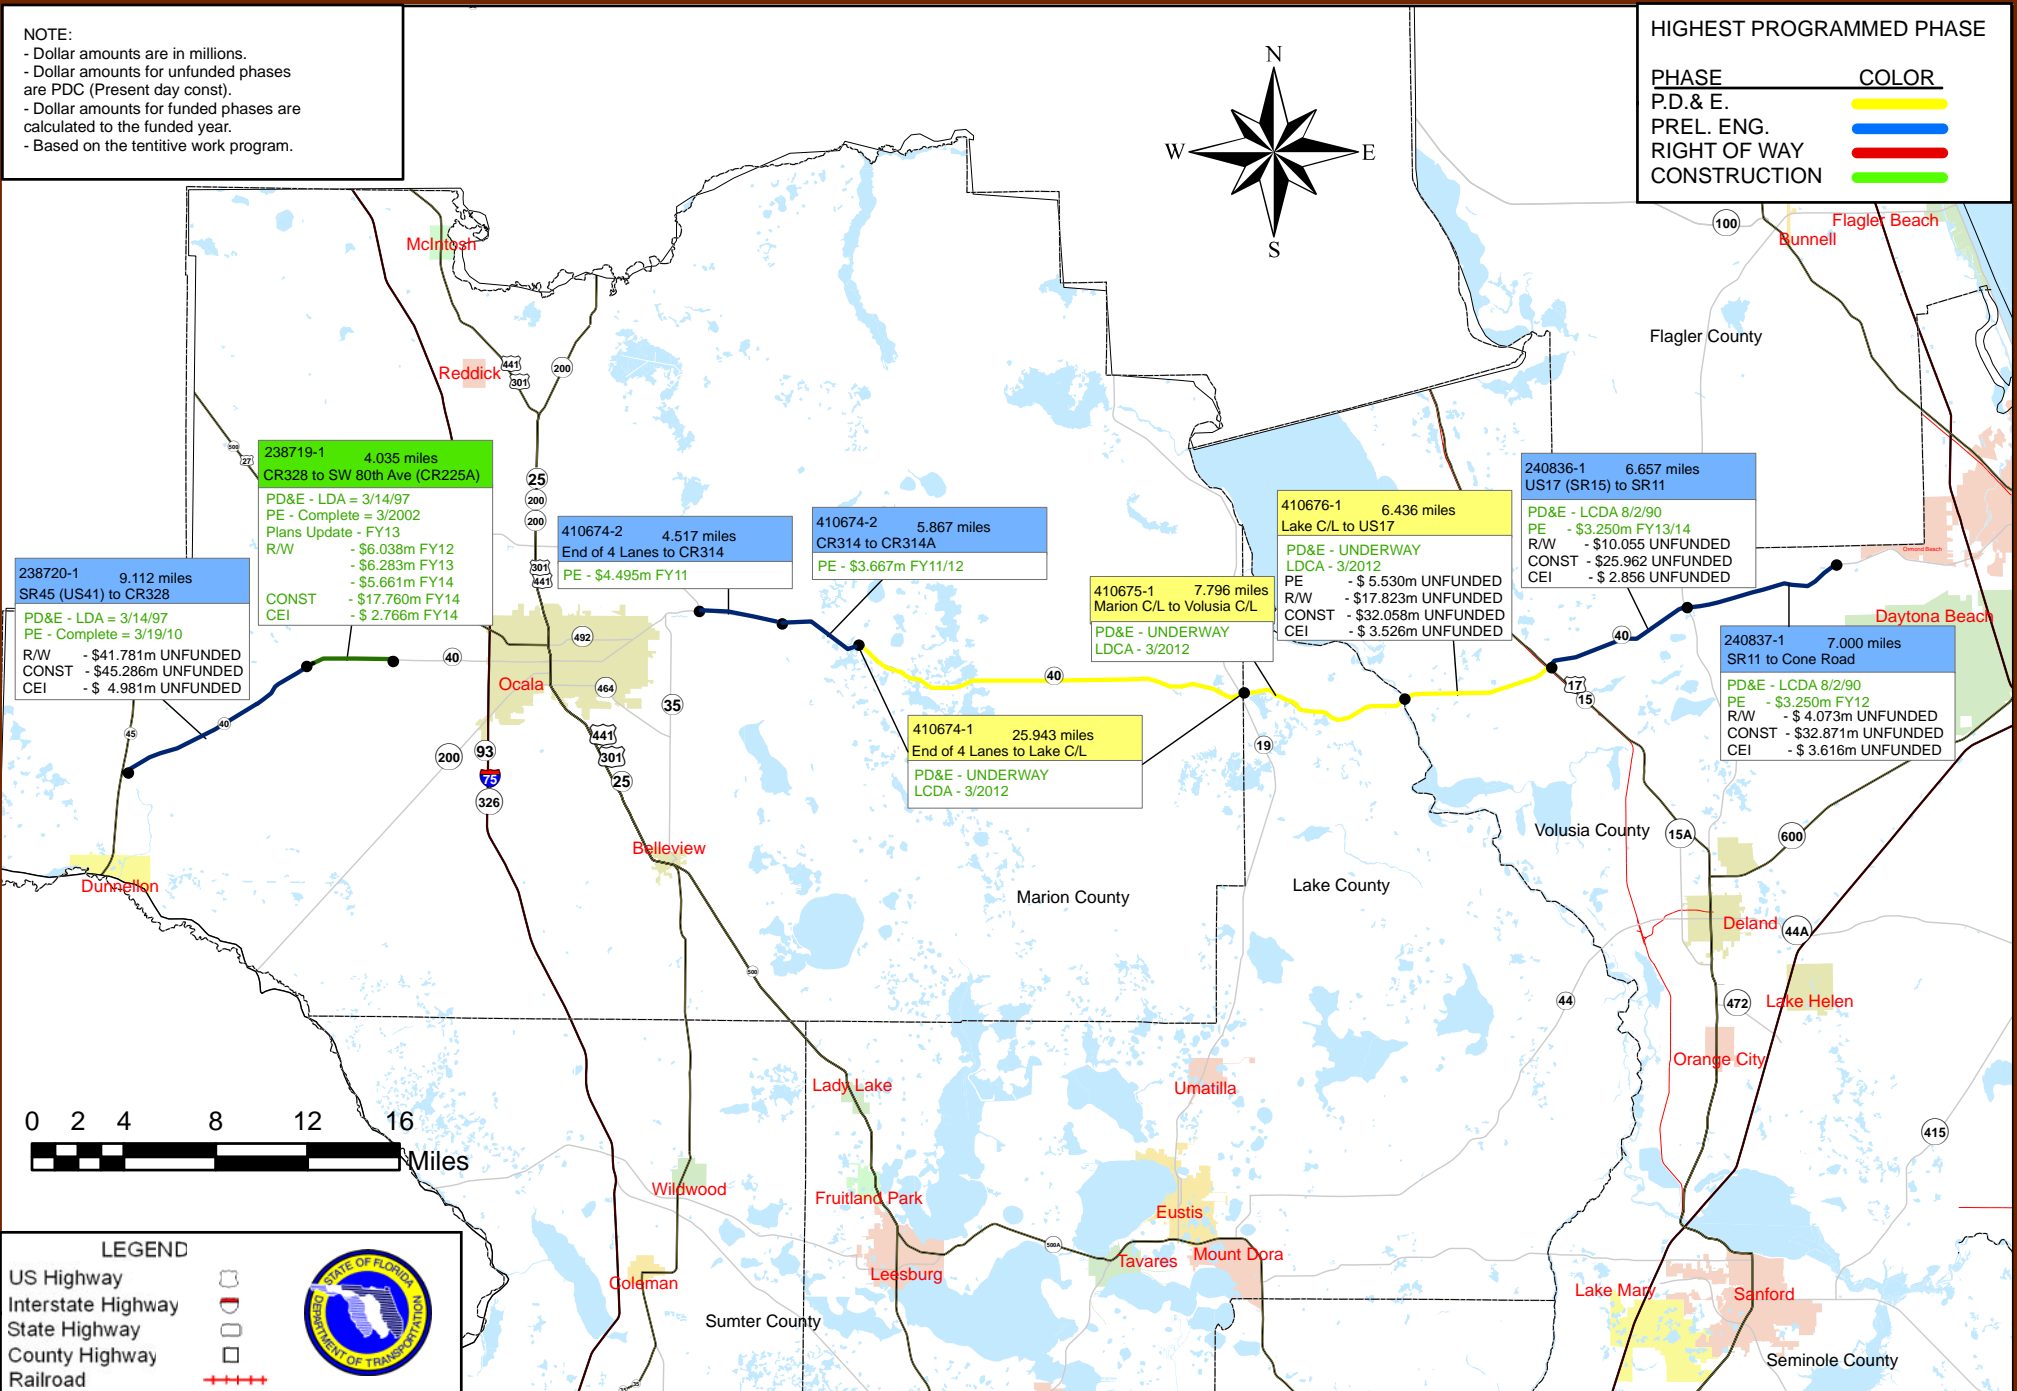

238720-1 9.112 miles
 SR45 (US41) to CR328
 PD&E - LDA = 3/14/97
 PE - Complete = 3/19/10
 R/W - \$41.781m UNFUNDED
 CONST - \$45.286m UNFUNDED
 CEI - \$ 4.981m UNFUNDED

238719-1 4.035 miles
 CR328 to SW 80th Ave (CR225A)
 PD&E - LDA = 3/14/97
 PE - Complete = 3/2002
 Plans Update - FY13
 R/W - \$6.038m FY12
 - \$6.283m FY13
 - \$5.661m FY14
 CONST - \$17.760m FY14
 CEI - \$ 2.766m FY14

410674-2 4.517 miles
 End of 4 Lanes to CR314
 PE - \$4.495m FY11

410674-2 5.867 miles
 CR314 to CR314A
 PE - \$3.667m FY11/12


410675-1 7.796 miles
 Marion C/L to Volusia C/L
 PD&E - UNDERWAY
 LDCA - 3/2012

410674-1 25.943 miles
 End of 4 Lanes to Lake C/L
 PD&E - UNDERWAY
 LDCA - 3/2012

410676-1 6.436 miles
 Lake C/L to US17
 PD&E - UNDERWAY
 LDCA - 3/2012
 PE - \$ 5.530m UNFUNDED
 R/W - \$17.823m UNFUNDED
 CONST - \$32.058m UNFUNDED
 CEI - \$ 3.526m UNFUNDED

240836-1 6.657 miles
 US17 (SR15) to SR11
 PD&E - LCDA 8/2/90
 PE - \$3.250m FY13/14
 R/W - \$10.055 UNFUNDED
 CONST - \$25.962 UNFUNDED
 CEI - \$ 2.856 UNFUNDED

240837-1 7.000 miles
 SR11 to Cone Road
 PD&E - LCDA 8/2/90
 PE - \$3.250m FY12
 R/W - \$ 4.073m UNFUNDED
 CONST - \$32.871m UNFUNDED
 CEI - \$ 3.616m UNFUNDED



LEGEND
 US Highway
 Interstate Highway
 State Highway
 County Highway
 Railroad

